

Operation Number:

TT-L1018

Year- PMR Cycle: Last Update:

First period Jan-Jun 2015

10/14/2015 PMR Validation Stage: Validated by Representative Chief of Operations validation date: Division Chief validation date:

Country Representative validation date:

10/14/2015 10/20/2015 11/13/2015 Office of Strategic Planning and Development Effectiveness

Inter-American Development Bank - IDB

Operation Profile

Basic Data

Operation name:	WASA Modernization and Wastewater Infrastructure Rehabilitation Program	Loan Number:	2600/OC-TT
Executing Agency (EA):	WATER AND SEWERAGE AUTHORITY		
Team Leader:	Cayetano,Evan Stephen	Sector/Subsector:	AS
Operation Type:	Loan Operation	Overall Stage:	Disbursing (From eligibility until all the loans are closed).
Lending Instrument:	Investment Loan	Country:	TRINIDAD AND TOBAGO
Borrower:	TRINIDAD AND TOBAGO	Convergence related Operation(s):	

Total Cost and Source

Available Funds (US\$)

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate		Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
TT-L1018	\$50,000,000.00	\$50,000,000.00	\$0.00	\$0.00	\$50,000,000.00	TT-L1018	\$50,000,000.00	\$20,144,648.08	40.29%	\$29,855,351.92


Environmental and Social Safeguards

	Main Operation
Impacts Category:	В
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	

Reformulation Information

	Main Operation
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

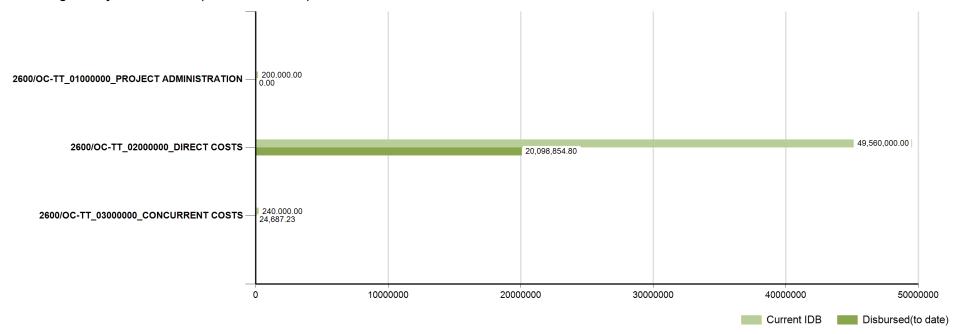

Results Matrix

Impacts

No information related to this operation.

ne:													
Observ tion:													
Indicators	F	lags*	Unit of Measure	Baseline	Baselin e Year	Means of verification	Observ ations		2013	2014	2015	2016	ЕОР
.1 Househo	ds					WASA		Р					10,000.00
in the program area covered						statistic		P(a)		0.00	0.00	9,100.00	9,100.00
y a centraliz			Household s	0.00	2012	and water quality		Α			0.00		
vastewater reatment ystems			5			monitoring reports							
.2 Average								Р					400.00
lifference of								P(a)		0.00	0.00	400.00	400.00
coliforms alues						WASA		Α			0.00		
ipstream)for Vastewater Treatment Plants in program area						monitoring reports							
.3 Estimate	t					WASA water		Р					0.00
otal daily verage								P(a)		0.00	0.00	110.00	110.00
vastewater			I					Α			0.00		
reated befor being lischarged ir he Caroni riv n program a	ı ver		l/sec	0.00	2012	quality monitoring reports							
Outco 2 \	VASA r	eorgani	zed										
bserv tion:													
Indicators	F	lags*	Unit of Measure	Baseline	Baselin e Year	Means of verification	Observ ations		2013	2014	2015	2016	ЕОР
.1 Number	of					WASA		Р					11.00
mployees p .000	er		Employees	13.00	2012	Human Resources		P(a)	12.00	11.00	0.00	11.00	11.00
onnection			Employees	13.00	2012	Division statistics		A	12.00	10.00	9.30		10.00
.2 Personne						WASA		Р					38.00
ost / operati xpenses	ng		%	50.00	2012	Finance Division		P(a)	44.00	38.00			38.00
APO11000						statistics		Α	44.00	41.60	40.30		41.60
			(in ORM on	d water auc	litu mani	toring) impro	ovod						

Indicators	Flags*	Unit of Measure	Baseline	Baselin e Year	Means of verification	Observ ations		2013	2014	2015	2016	EOP
3.1 Wastewater					\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\\		Р					90.00
physical assets in good conditions in					WASA Maintenan		P(a)		0.00	0.00	90.00	90.00
		%	5.00	2012	ce Team report		Α			0.00		
the program area												
3.2 Wastewater							Р					90.00
quality samples						P(a)		0.00	0.00	90.00	90.00	
complying with effluent				2012	WASA monitoring reports		Α			0.00		
standards for rehabilitated plants in program area		%	0.00									

Outputs: Annual Physical and Financial Progress

Vastewater management system in Trinidad improved					Financial Progress			
Unit of Measure		2015	EOP		2015	EOP		
Plants	Р	1.00	4.00	Р	5,063,000.00	16,968,900.00		
	P(a)	0.00	4.00	P(a)	0.00	17,529,398.00		
	Α		0.00	Α	0.00	31,200.00		
Plant	Р	1.00	7.00	Р	306,000.00	1,863,000.00		
	P(a)	0.00	7.00	P(a)	0.00	1,863,000.00		
	Α		0.00	Α	0.00	0.00		
km	Р	3.00	10.00	P	1,085,700.00	6,753,500.00		
	P(a)	0.00	10.00	P(a)	0.00	6,753,000.00		
	Α		0.00	Α	0.00	0.00		
km	Р	0.00	3.00	Р	172,200.00	1,343,640.00		
	P(a)	0.00	3.00	P(a)	0.00	1,343,640.00		
	Α		0.00	Α	0.00	0.00		
	F	Physical Progress			Financial Progress			
Unit of Measure		2015	EOP		2015	EOP		
Employees	Р		550.00	Р		20,113,000.0		
	P(a)		872.00	P(a)		20,113,202.0		
	Α	83.00	955.00	Α	0.00	20,113,202.0		
ality monitoring)	Physical Progress			Financial Progress				
Unit of Measure		2015	EOP		2015	EOP		
Plan	Р		1.00	Р		50,000.00		
	P(a)	0.00	1.00	P(a)	0.00	50,000.00		
	Α		0.00	Α	0.00	0.00		
Staff-month	Р	15.00	45.00	Р	66,670.00	200,010.00		
	P(a)	0.00	45.00	P(a)	0.00	200,010.00		
	A		0.00	Α	0.00	0.00		
Plan	Р	1.00	4.00	Р	65,000.00	260,000.00		
	P(a)	3.00	4.00	P(a)	0.00	260,000.00		
	Α	0.00	0.00	Α	0.00	63,650.3		
Staff-Month	Р	5.00	5.00	Р		40,000.00		
Staff-Month								
Staff-Month	P(a)	1.00	5.00	P(a)	12,000.00	40,000.00		
	Unit of Measure Plants Plant km Unit of Measure Employees ality monitoring) Unit of Measure Plan	Unit of Measure	Unit of Measure	Unit of Measure 2015 EOP Plants P 1.00 4.00 P(a) 0.00 4.00 A 0.00 7.00 P(a) 0.00 7.00 A 0.00 10.00 P(a) 0.00 10.00 P(a) 0.00 3.00 P(a) 0.00 3.00 P(a) 0.00 3.00 Physical Progress P 550.00 P(a) 872.00 872.00 A 83.00 955.00 Plan Physical Progress Unit of Measure 2015 EOP Plan P(a) 0.00 1.00 A 0.00 1.00 4.00 P(a) 0.00 45.00 P(a) 0.00 40.00 <td> Note of Measure 2015 EOP </td> <td> Unit of Measure</td>	Note of Measure 2015 EOP	Unit of Measure		

Other Cost		2015	Cost
Project administration	Р	\$40,000.00	\$200,000.00
	P(a)	\$0.00	\$200,000.00
	Α	\$0.00	\$0.00
Auditing	Р	\$30,000.00	\$150,000.00
	P(a)	\$25,000.00	\$150,000.00
	Α	\$0.00	\$24,687.23
Work supervision	P	\$333,000.00	\$1,332,000.00
	P(a)	\$50,000.00	\$1,332,000.00
	Δ	\$46,300,00	\$77,500,00

Project standard information campaign	P	\$19,000.00	\$75,750.00
	P(a)	\$0.00	\$75,750.00
	Α	\$0.00	\$0.00
Monitoring and Evaluation	P	\$7,500.00	\$90,000.00
	P(a)	\$7,500.00	\$90,000.00
	Α	\$0.00	\$0.00
Total Cost		2015	Total Cost
	Р	\$7,188,070.00	\$49,439,800.00
	P(a)	\$94,500.00	\$49,951,800.00
	Α	\$46,300.00	\$20,321,870.37

Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report's publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
