




Summary Report


Basic Data		Available Funds (US\$)		Total Cost and Source	
Executing Agency (EA):	SECRETARIA MUNICIPAL DE HABITACION				
Sector:	URBAN DEVELOPMENT AND HOUSING-INTEGRATED URBAN DEVELOPMENT				
Loan Number(s):	2482/OC-BR	Current Approved Amount:	150.000.000,00	Original IDB:	150.000.000,00
Stage:	Approved	Disbursed Amount to Date:		Current IDB:	150.000.000,00
Operation Type:	INV - Investment	% Disbursed:		Pari-passu:	
Related Operation(s):	BR-T1131, RG-P1374, RG-P1400	Balance:	150.000.000,00	Co-Financing/Country:	150.000.000,00
Operation Subtype:	GOM - Global of Multiple Works Operation			Original Estimate:	300.000.000,00
				Amortization Period (months):	

Project Environmental and Social Impact Category	Reformulation	Validation
Project Environmental and Social Impact Category: B	() Was the objective(s) of this project reformulated?	Validated by Division Chief: Mar 30, 2011 Validated by Country Representative: Apr 20, 2011

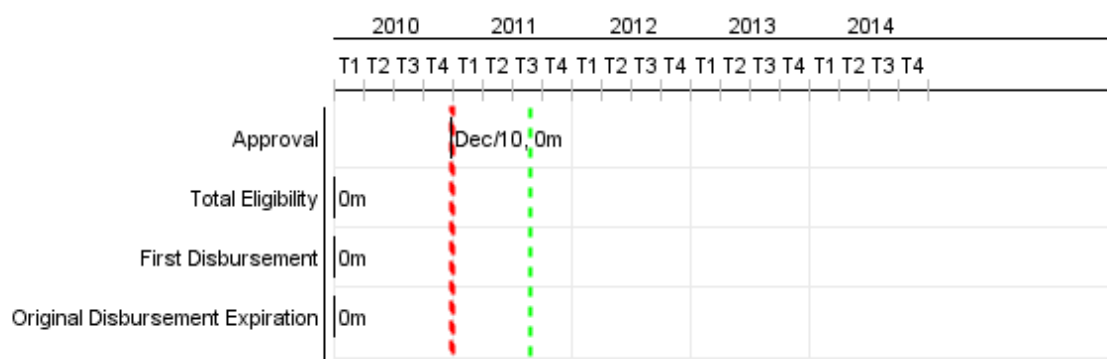

Accumulated Progress as of 2010

Accumulated Progress



PROGRESS MONITORING REPORT

BR-L1175 - Rio de Janeiro Low-income Neighborhood Urban Development Program -
Stage III
2010 2° period with closure up to(31-Mar-2011)

Inter-American Development Bank - IDB
Office of Strategic Planning and Development Effectiveness

Last Update: 21/03/2011

Outcomes

Outcome: Nivel de desarrollo socio económico de las comunidades intervenidas mejorado

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Indice de Desarrollo Social Ampliado	Indice	47,00	2005	P A	57,00

Outcome: Formación/generación de activos en las comunidades intervenidas incrementado

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Valor por metro cuadrado en area construidas	R\$/m2	235,00	2008	P A	430,00

Outcome: Comunidades intervenidas integradas a la ciudad formal

Indicator	Unit of Measure	Baseline	Baseline Year		End of project
Índice de Integración Urbana ampliado	Indice	56,00	2005	P A	74,00

Outputs: 2010 Annual Physical and Financial Progress 2010

Description	Unit of Measure	Physical				Financial			
		Planned	Actual	Accumulated units	EOP units	Planned	Actual	Accumulated costs	EOP costs
Urbanización Integrada									
Proyectos Integrales Realizados en Favelas	Favelas urbanizadas				30,00				196.500.000,00
Infraestructura y servicios sociales implantados en Loteamientos	Loteamientos				6,00				18.000.000,00
Acciones Sociales									
Centros de Educación Infantil Construidos	Centro				28,00				8.300.000,00
CRAS - Centros de referencia en Acciones Sociales Operando	Centros o Unidades Muebles				12,00				3.500.000,00
Apoyo a Jóvenes en Situación de Riesgo	Centros Apoyados				5,00				10.700.000,00
Trabajo e Ingreso	Acciones realizadas				5,00				1.000.000,00
Regularización y Control Urbanístico									
Sistema de Controle da Ocupação del Suelo Implantado	Sistema				1,00				5.500.000,00
POUSOS (Puestos de Orientación Urbanística y Social en Operación)	POUSO				24,00				7.700.000,00
Regularización Urbanística Realizada	Inmuebles				10.000,00				4.800.000,00
Monitoreo y Capacitación									
Técnicos Municipales Capacitados (seminarios, asistencia técnica, comunicación)	Técnicos				30,00				1.350.000,00
Evaluación Realizada	Evaluación				2,00				2.000.000,00
Outros									
Gerenciamiento, Proyectos y Auditoría Realizados	Gerenciamiento y Proyectos				4,00				23.450.000,00
Gastos Financieros Realizados	Gastos financieros				1,00				17.200.000,00
TOTAL									300.000.000,00
