



Operation Number: **CH-L1032**
Year- PMR Cycle: **Segundo período enero-diciembre 2013**
Last Update: **6/6/2014**
PMR Validation Stage: **Validada por el Representante de País**

Chief of Operations validation date: **06/20/2014**
Division Chief validation date: **06/23/2014**
Country Representative validation date: **07/01/2014**

Inter-American Development Bank - IDB
Office of Strategic Planning and Development Effectiveness

Operation Profile

Basic Data

Operation name:	Programa de Puesta en Valor del Patrimonio (CCLIP)	Loan Number:	1952/OC-CH
Executing Agency (EA):	SUBSECRETARIA DE DESARROLLO REGIONAL- MINTER		
Team Leader:	Adler,Veronica	Sector/Subsector:	URBAN REHABILITATION AND HERITAGE
Operation Type:	Loan Operation	Overall Stage:	Cerrado (Todos los préstamos están cerrados)
Lending Instrument:	Investment Loan	Country:	CHILE
Borrower:	REPUBLICA DE CHILE	Convergence related Operation(s):	

Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
CH-L1032	\$80,000,000.00	\$80,000,000.00	\$20,000,000.00	\$0.00	\$100,000,000.00

Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
CH-L1032	\$80,000,000.00	\$48,000,000.00	60.00%	\$32,000,000.00


Environmental and Social Safeguards

Main Operation	
Impacts Category:	B13
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	

Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

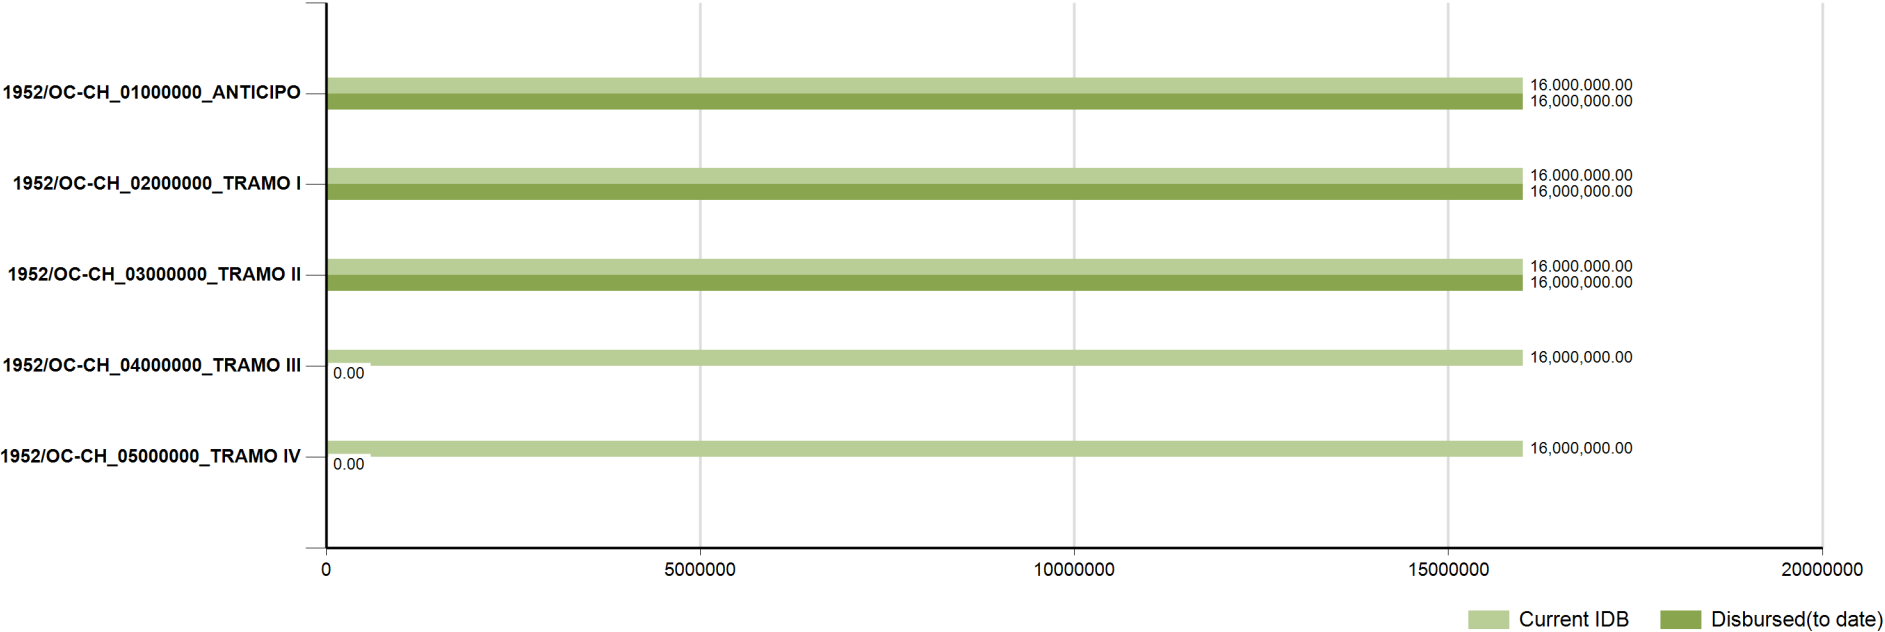

 RF - RF Indicator  SI - Sector Indicator  CI - Country Indicator  PG - Pro-Gender  PE - Pro-Ethnicity

Outputs: Annual Physical and Financial Progress

Protección y puesta en valor del patrimonio		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2013		EOP	2013		EOP
Obras de Bienes patrimoniales terminadas	bienes patrimoniales	P		11.00	P		
		P(a)	12.00	49.00	P(a)		0.00
		A		49.00	A		
Fortalecimiento institucional		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2013		EOP	2013		EOP
Planes de gestión de bienes patrimoniales puestos en vigencia	Planes de gestión	P		3.00	P		
		P(a)	18.00	34.00	P(a)	40.00	0.00
		A		34.00	A		
Metodología de evaluación elaborada	Metodología	P		1.00	P		
		P(a)		0.00	P(a)		0.00
		A		0.00	A		
Total Cost					2013		Total Cost
				P			
				P(a)	\$40.00		\$40.00
				A			

Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report’s publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
