


PMR Public Report

Operation Number	GU-L1039	Chief of Operations Validation Date	10/12/22
Year- PMR Cycle	First period Jan-Jun 2022	Division Chief Validation Date	
Last Update	10/11/22	Country Representative Validation Date	
PMR Validation Stage	Validated by Chief of Operations		
Basic Data			
Operation Profile			
Operation Name	Water and Sanitation Program for Human Development-Phase I	Loan Number	2242/BL-GU, 2242/BL-GU-1
Executing Agency	SECRETARIA GENERAL DE LA PRESIDENCIA, INSTITUTO DE FOMENTO MUNICIPAL	Sector/Subsector	WATER AND SANITATION
Team Leader	GOBITZ, HUMBERTO A.	Overall Stage	Disbursing (From eligibility until all the Operations are closed)
Operation Type	Loan Operation	Country	Guatemala
Lending Instrument	Investment Loan	Convergence related Operation(s)	GU-X1005
Borrower	REPUBLICA DE GUATEMALA		
Environmental and Social Safeguards			
Impacts Category	B	Was/Were the objective(s) of this operation reformulated?	NO
Safeguard Performance Rating	Partially Satisfactory	Date of approval	
Safeguard Performance Rating - Rationale	Se ha mejorado la gestión socioambiental, sin embargo, se mantiene el desempeño en PS debido a que no se ha completado la Gestión de derechos de paso, asunto que se mantiene desde la misión anterior y que por contrato debía estar finiquitado antes de iniciar las obras. Además, existen conflictos con la comunidad de San Pedro Sacatepéquez debido a quejas por la pavimentación de las calles después de finalizadas las obras. Está pendiente igualmente la entrega un informe de corta de árboles y compensación forestal, en especial clarificando el tipo de ecosistema natural que se está interviniendo en San Pedro Sacatepequez.		

Financial Data									
	Total Cost and Source					Available Funds (US\$)			
Operations	Original IDB	Current IDB	Local Counterpart	Co-Financing / Country	Total Original Cost	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Amount
GU-L1039	50,000,000	50,000,000	0	0	50,000,000	50,000,000	47,800,000	95.60%	2,200,000
GU-X1005	50,000,000	50,000,000	0	0	50,000,000	50,000,000	42,000,000	84.00%	8,000,000
Aggregated	100,000,000	100,000,000	0	0	100,000,000	100,000,000	89,800,000	89.80%	10,200,000
Expense Categories by Loan Contract (cumulative values)									

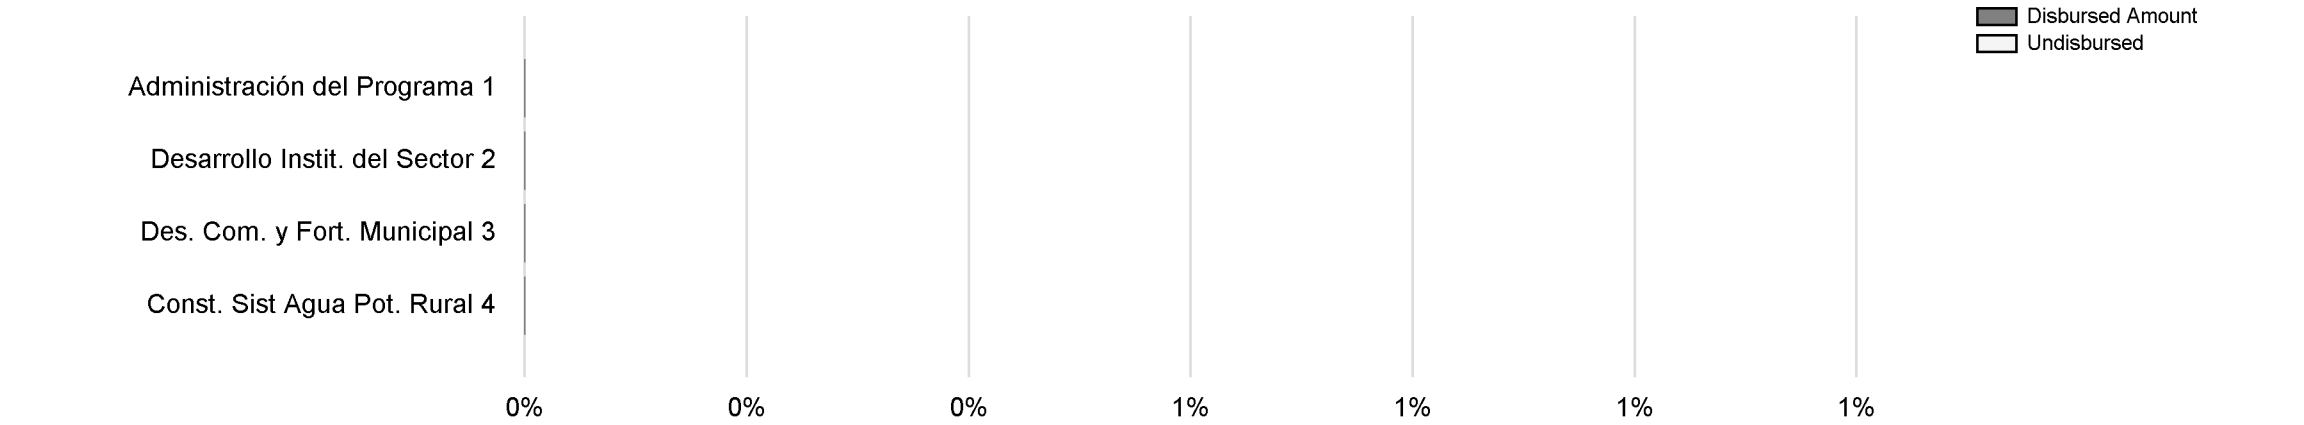

Please note that inactive indicators and outputs are not displayed; totals in the actual cost table may not match the sum of the cost of the outputs displayed, due to the cost of inactive outputs.

RESULTS MATRIX
General Development Objectives

RESULTS MATRIX																
Specific Development Objectives																
Specific Development Objectives Nbr. 1: Plan de Consolidación Institucional del Ministerio de Salud Publica y asistencia Social -MSPAS-, en temas de rectoría, regulación y planificación de prestación de servicios de agua potable y saneamiento implementada																
Observation:																
	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
1.1	Rectoria sectorial fortalecida y funcionando	Entidades	0	2012	P	-	-	-	-	1	-	-	-	-	-	1
					A	-	-	-	-	-	-	-	-	-	-	
Details																
Means of Verification: Documentos Legales del Ministerio de Salud creando la direccion de Direccion de agua potable y saneamiento, para ejercer la rectoria del sector.																
Observations:																
Evaluation Methodology: -																
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator												
Specific Development Objectives Nbr. 2: Unidad especializada en el desarrollo de Programas de agua potable y saneamiento instituida en el Gobierno Central																
Observation:																
	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
2.1	Entidad ejecutora de Programas sectoriales autonoma funcionando	Entidad	0	2012	P	-	-	-	-	1	-	-	-	-	-	1
					A	-	-	-	-	-	-	-	-	-	-	
Details																
Means of Verification: Informe de desempeño del Programa a los 5 años de la firma del contrato del contrato de préstamo o cuando se hayan alcanzado el 75 % de avance.																
Observations:																
Evaluation Methodology: -																
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator												
Specific Development Objectives Nbr. 3: Cobertura servicios de agua potable y saneamiento autosostenibles ,incrementada la República de Guatemala																
Observation:																
	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
3.1	Hogares rurales con sistema de agua potable contruídos o rehabilitados	# of households	0	2012	P	200	4,600	4,600	4,700	4,160	-	-	-	-	-	18,260
					A	42	745	789	-	1,311	3,206	1,595	-	4,092	-	7,688
Details																
Means of Verification: Informes de SEGEPLAN, y de los entes rector y ejecutor del sector																
Observations: En la matriz de resultado original, se habían expresado los resultados en forma de porcentaje y número de beneficiarios, por lo que se ha utilizado la ponderación de hogares en función de la tasa promedio definida por la Encuesta Nacional de Vivienda 2011																
Evaluation Methodology: -																
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	2.4.a Households with improved access to water (#) (C)											
	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
3.1	Hogares periurbanos y urbanos con solución de agua potable construídos o rehabilitados	# of households	0	2012	P	-	-	6,000	15,000	5,000	-	-	-	-	-	26,000
					A	-	-	-	-	-	-	982	-	815	-	982
Details																
Means of Verification: Informes de SEGEPLAN, y de los entes rector y ejecutor del sector																
Observations:																
Evaluation Methodology: -																
Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	2.4.a Households with improved access to water (#) (C)											

[illegible]

Details

Means of Verification: Informes de SEGEPLAN, y de los entes rector y ejecutor del sector

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	2.4.b Households with improved access to sanitation (#) (C)

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
3.4	Hogares periurbanos y urbanos con solución de alcantarillado construídos o rehabilitados	# of households	0	2012	P	-	-	9,000	18,000	7,000	-	-	-	-	-	34,000
					A	-	-	-	-	-	-	982	-	1,763	-	982

Details

Means of Verification: Informes de SEGEPLAN, y de los entes rector y ejecutor del sector

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	2.4.b Households with improved access to sanitation (#) (C)

	Indicator	Unit of Measure	Baseline	Baseline Year		2013	2014	2015	2016	2017	2018	2019	2020	2021	2022	EOP 2023
3.4	Hogares cuyas aguas residuales son tratadas	# of households	0	2014	P	-	-	-	-	-	-	-	-	-	-	-
					A	-	-	-	-	-	-	982	-	1,763	-	982

Details

Means of Verification:

Observations:

Evaluation Methodology: -

Pro-Gender	No	Pro-Ethnicity	No	CRF indicator	2.4.b Households with improved access to sanitation (#) (C)

RESULTS MATRIX

OUTPUTS: ANNUAL PHYSICAL AND FINANCIAL PROGRESS

Component Nbr. 1 Componente 1. Desarrollo Institucional del Sector

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2023	2022	EOP 2023
1.01	Entidad Rectora Sectorial de agua y saneamiento funcionando	Entidad	P	-	1	-	1,500,000
			P (a)	-	-	1,500,000	1,500,000
			A	-	-	-	-
1.02	Entidad ejecutora especializada del sector de agua y saneamiento funcionando	Entidad	P	-	1	-	1,500,000
			P (a)	-	-	-	1,127,664
			A	-	-	-	1,127,664
1.03	Entidad rectora de la calidad de agua para consumo humano fortalecida	Entidad	P	-	1	-	700,000
			P (a)	1	1	700,000	700,000
			A	-	-	8,887	8,887

Component Nbr. 2 Componente 2. Inversiones en Infraestructura

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2023	2022	EOP 2023
2.01	Sistemas de agua potable y/o saneamiento rurales diseñados	Sistemas	P	-	335	-	3,400,000
			P (a)	-	46	-	9,604
			A	-	46	-	9,604
2.02	Sistemas de agua potable y/o saneamiento diseñados en comunidades urbanos	Sistemas	P	-	32	-	3,000,000
			P (a)	-	17	-	886,085.03
			A	-	17	-	886,085.03
2.03	Sistemas rurales de agua potable contruidos o rehabilitados	Sistemas	P	-	220	-	34,908,000
			P (a)	3	59	414,241	21,437,717.92
			A	-	56	460,819	21,484,295.92
2.04	Sistemas rurales con solución de saneamiento básico construidos o rehabilitados	Sistemas	P	-	280	-	23,272,000
			P (a)	2	78	276,160	9,237,816.24
			A	-	76	19,411	8,981,067.24
2.05	Sistemas periurbanos y urbanos con solución de agua potable construídos o rehabilitados	Sistemas	P	-	32	-	13,272,000
			P (a)	5	9	6,304,756	22,242,657.16
			A	-	4	1,865,953	17,803,854.16
2.06	Sistemas periurbanos y urbanos con solución de alcantarillado construídos o rehabilitados	Sistemas	P	-	32	-	8,848,000
			P (a)	5	10	9,647,912	35,967,044.85
			A	-	5	4,769,510	31,088,642.85

Component Nbr. 3 Componente 3. Desarrollo Comunitario y fortalecimiento Municipal para la prestación de servicios de agua y saneamiento

				PHYSICAL PROGRESS		FINANCIAL PROGRESS	
	Output	Unit of Measure		2022	EOP 2023	2022	EOP 2023
3.01	Organizaciones comunitarias rurales sosteniendo los sistema de agua y saneamiento	Organización	P	-	280	-	4,000,000
			P (a)	3	116	22,054	1,134,946.55
			A	-	113	6,549	1,119,441.55
3.02	Personas de Comunidades Rurales capacitadas en educación sanitaria y ambiental	Personas	P	-	84,000	-	1,000,000
			P (a)	50	60,558	21,045	982,306.72
			A	-	60,508	6,549	967,810.72
3.03	Gobiernos municipales fortalecidos en prestación de servicios de agua potable y saneamiento	Government agencies (#)	P	-	32	-	1,500,000
			P (a)	5	9	40,255	287,369.65
			A	-	4	54,896	302,010.65
3.04	Personas de la municipalidad capacitadas	Personas	P	-	320	-	500,000
			P (a)	50	90	40,540	281,497.69
			A	10	50	35,849	276,806.69

Component Nbr. 4 Administración del programa

				FINANCIAL PROGRESS
	Output	Unit of Measure		EOP
4.00			P	-
			P (a)	-
			A	-

Other Cost				
	Administración del Programa	P		2,600,000
		P (a)	317,900.7	4,205,290.19
		A	185,301	4,072,690.49
Total Cost				
	Total Cost	P	0	100,000,000
		P (a)	19,284,863.7	100,000,000
		A	7,413,724	88,128,860.3

No information available for this section

RISKS AND PLANNED RESPONSES

Risk ID	Risk Status		Risk Taxonomy		
3	Active		Planning		
	Response Actions				
	3.1	Management Strategy		Status	
		ACCEPT		ACTIVE	
	3.2	Management Strategy		Status	
		MITIGATE		COMPLETE	

Risk ID	Risk Status		Risk Taxonomy		
6	Inactive		Natural Environment		
	Response Actions				
	6.1	Management Strategy		Status	
		ACCEPT		COMPLETE	
	6.2	Management Strategy		Status	
		TRANSFER		ACTIVE	

Risk ID	Risk Status		Risk Taxonomy		
9	Active		Institutional Environment		
	Response Actions				
	9.1	Management Strategy		Status	
		TRANSFER		ACTIVE	
	9.2	Management Strategy		Status	
		MITIGATE		ACTIVE	

Risk ID	Risk Status		Risk Taxonomy		
12	Active		Institutional Environment		
	Response Actions				
	12.1	Management Strategy		Status	
		ACCEPT		ACTIVE	
	12.2	Management Strategy		Status	
		TRANSFER		ACTIVE	

IMPLEMENTATION STATUS AND LEARNING

Lesson Learned - Categories
Project Management Capacity
