



Operation Number: **JA-L1037**
Year- PMR Cycle: **First period Jan-Jun 2016**
Last Update: **10/12/2016**
PMR Validation Stage: **Validated by Chief of Operations**

Chief of Operations validation date: **10/18/2016**
Division Chief validation date:
Country Representative validation date:

Inter-American Development Bank - IDB
Office of Strategic Planning and Development Effectiveness

Operation Profile

Basic Data

Operation name:	Integrated Social Protection and Labor Program	Loan Number:	2889/OC-JA
Executing Agency (EA):	MINISTRY OF LABOUR AND SOCIAL SECURITY		
Team Leader:	Harris,Donna Oretha	Sector/Subsector:	POVERTY ALLEVIATION
Operation Type:	Loan Operation	Overall Stage:	Disbursing (From eligibility until all the Operations are closed)
Lending Instrument:	Investment Loan	Country:	JAMAICA
Borrower:	JAMAICA	Convergence related Operation(s):	

Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
JA-L1037	\$30,000,000.00	\$30,000,000.00	\$0.00		\$30,000,000.00

Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
JA-L1037	\$30,000,000.00	\$28,267,818.91	94.23%	\$1,732,181.09


Environmental and Social Safeguards

Main Operation	
Impacts Category:	C
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	

Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

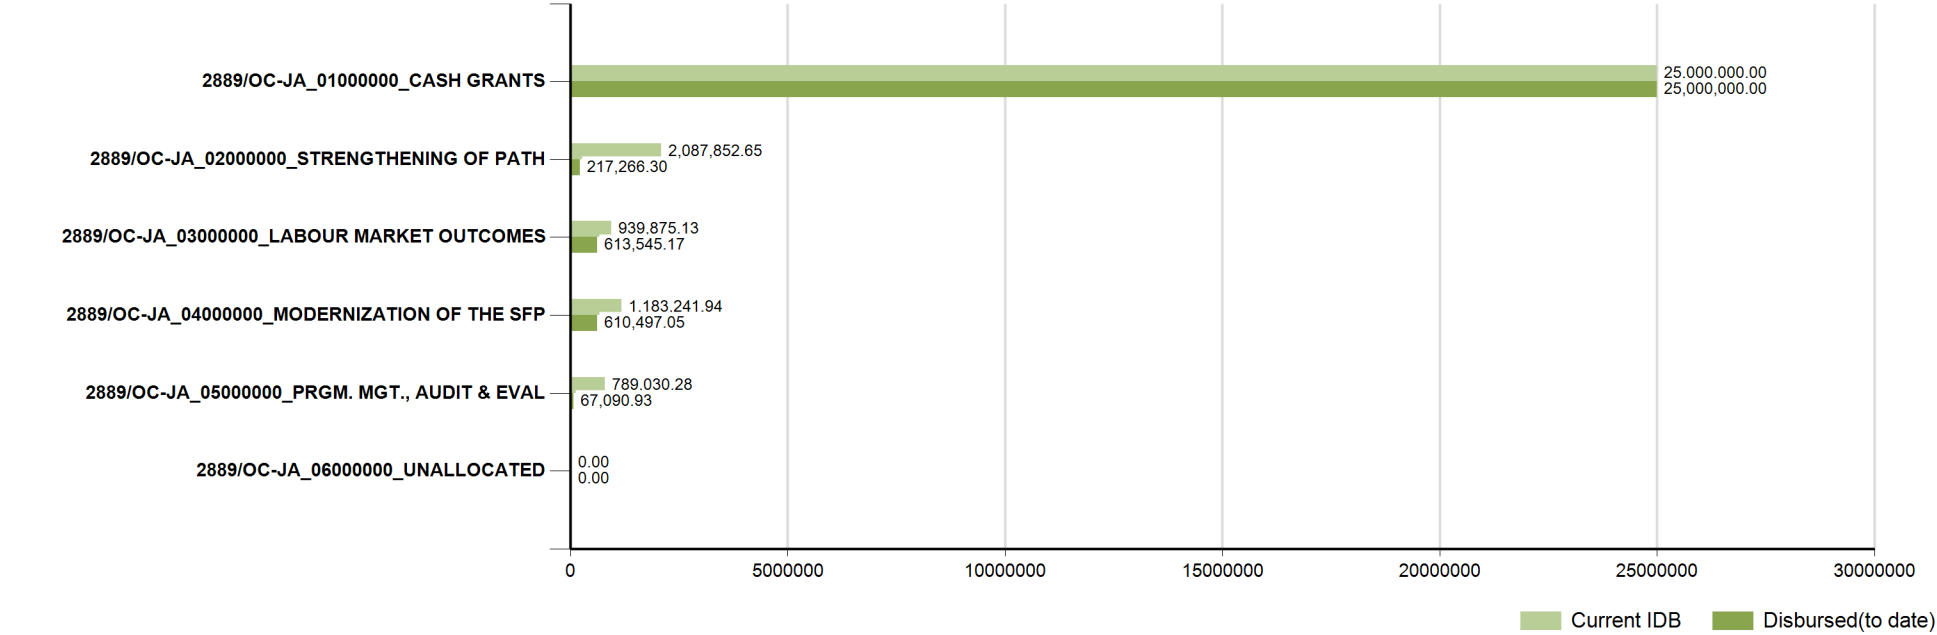

Results Matrix

Impacts

Impact:	1 Increased compliance of full set of health conditionalities for 2-6 years							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
1.1 increased coverage		percentage	55.00	2013	PATH BMIS	Referred to communities participating in parenting education condition	P	75.00
							P(a)	75.00
							A	0.00



RF - Contribution



RF - Alignment



RF - Strategic Alignment



RF - Strategic Alignment during Execution



SI - Sector Indicator



CI - Country Indicator



PG - Pro-Gender



PE - Pro-Ethnicity

Outcomes

Outcome:	1 Improved parenting skills									
Observation:										
							2015	2017	EOP	
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations				
1.1 Percentage of parents that do not approve violent discipline		percentage	10.00	2013	Impact evaluation of pilot of new parenting conditions		P			50.00
	P(a)								50.00	
	A			0.00						
3.0 Parenting skills as measured by the average test in parenting skills		percent	20.00	2014	Impact evaluation and PATH BMIS		P			
	P(a)								30.00	
	A			0.00						
Outcome:	2 Employment outcomes for PATH beneficiaries									
Observation:										
							2015	2017	EOP	
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations				
2.1 Number of PATH beneficiaries employed six months after completion of on the job steps to work training		beneficiaries	0.00	2013	PATH BMIS		P			600.00
	P(a)						150.00		600.00	
	A	0.00		0.00						
Outcome:	3 Electronic labour exchange updated and improved									
Observation:										

Outco	3 Electronic labour exchange updated and improved
--------------	---

Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	2015		2017	EOP
3.1 Share of PATH individuals in verified employment within 1-6 months of ELE referral		percentage	0.00	2013	PATH BMIS and ELE		P			35.00
							P(a)			35.00
							A			0.00

-  RF - Contribution
-  RF - Alignment
-  RF - Strategic Alignment
-  RF - Strategic Alignment during Execution
-  SI - Sector Indicator
-  CI - Country Indicator
-  PG - Pro-Gender
-  PE - Pro-Ethnicity

Outputs: Annual Physical and Financial Progress

Component 1: PATH Cash Grants		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2016		EOP	2016		EOP
Coverage of beneficiaries (children and pregnant and lactating women)	Beneficiaries (#)	P	0.00	1,256,000.00	P	0.00	20,000,000.00
		P(a)	0.00	1,256,000.00	P(a)	0.00	25,000,000.00
		A	0.00	1,256,000.00	A	0.00	25,000,000.00
Component 2: Strengthening of PATH		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2016		EOP	2016		EOP
households participating in parenting education workshop pilot	households	P	5,000.00	10,000.00	P	575,000.00	1,150,000.00
		P(a)	500.00	500.00	P(a)	265,605.00	285,000.00
		A	600.00	600.00	A	26,478.47	45,873.47
Social messages about parenting delivered via SMS	social messages	P	100,000.00	250,000.00	P	87,500.00	250,000.00
		P(a)	175,000.00	175,000.00	P(a)	150,000.00	150,000.00
		A	0.00	0.00	A	0.00	0.00
Strengthening of PATH services to children with disabilities. Early stimulation program building facilities rehabilitated and upgraded	building	P	1.00	1.00	P	200,000.00	1,000,000.00
		P(a)	1.00	1.00	P(a)	1,136,989.00	1,170,000.00
		A	1.00	1.00	A	190,231.73	223,242.73
Alternative payment delivery systems assessed	system	P	1.00	1.00	P	100,000.00	300,000.00
		P(a)	1.00	1.00	P(a)	132,028.81	132,852.65
		A		0.00	A	0.00	823.84
PATH MIS upgraded	MIS system	P		1.00	P	100,000.00	350,000.00
		P(a)		1.00	P(a)	350,000.00	350,000.00
		A		0.00	A	338.93	338.93
Component 3: Improving labour market outcomes		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2016		EOP	2016		EOP
PATH Individual referred to jobs through the electronic labour exchange	beneficiaries	P		0.00	P		0.00
		P(a)	350.00	543.00	P(a)	0.00	0.00
		A	192.00	385.00	A		0.00
PATH beneficiaries participating in STW on the job training pilot	bebeneficiaries	P	600.00	1,500.00	P	756,500.00	1,963,000.00
		P(a)	350.00	473.00	P(a)	319,346.00	363,000.00
		A	192.00	315.00	A	123,155.38	166,809.38
Electronic labour exchange satellite offices and private sector office strengthened	offices	P	3.00	12.00	P	334,300.00	1,337,000.00
		P(a)	3.00	8.00	P(a)	264,450.68	437,000.00
		A	2.00	7.00	A	205,480.00	378,029.32
national employment policy completed	policy	P	1.00	1.00	P	76,000.00	276,000.00
		P(a)	1.00	1.00	P(a)	139,819.28	139,875.13
		A	0.00	0.00	A	0.00	55.85
Component 4: Modernization of the School Feeding Program		Physical Progress			Financial Progress		
Outputs	Unit of Measure	2016		EOP	2016		EOP
SFP MIS upgraded	MIS system	P		1.00	P		754,000.00
		P(a)		1.00	P(a)	707,993.82	713,241.94
		A		1.00	A		5,248.12
School Feeding Strategy and policy framework completed	policy	P		1.00	P		270,000.00
		P(a)		1.00	P(a)	1,301.98	270,000.00
		A		1.00	A		268,698.02

SFP operations manual completed	operations manual	P	1.00	1.00	P	200,000.00	200,000.00
		P(a)	1.00	1.00	P(a)	200,000.00	200,000.00
		A	1.00	1.00	A		0.00
Component 5: Program management, audit and evaluation							
Component 6: Unallocated							

Other Cost		2016	Cost
program management	P	\$465,000.00	\$1,050,000.00
	P(a)	\$144,118.78	\$164,030.28
	A	\$51,498.52	\$71,410.02
Contingency	P	\$250,000.00	\$250,000.00
	P(a)	\$0.00	\$0.00
	A	\$0.00	\$0.00
process and impact evaluation of parenting education/revised health condition	P	\$320,000.00	\$350,000.00
	P(a)	\$325,000.00	\$325,000.00
	A	\$0.00	\$0.00
On the job training process and impact evaluation	P	\$320,000.00	\$350,000.00
	P(a)	\$200,000.00	\$200,000.00
	A	\$0.00	\$0.00
Evaluation of new technologies	P	\$50,000.00	\$50,000.00
	P(a)	\$0.00	\$0.00
	A	\$0.00	\$0.00
Financial audit	P	\$100,000.00	\$100,000.00
	P(a)	\$100,000.00	\$100,000.00
	A		\$0.00
Total Cost		2016	Total Cost
	P	\$3,934,300.00	\$30,000,000.00
	P(a)	\$4,436,653.35	\$30,000,000.00
	A	\$597,183.03	\$26,160,529.68

Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report's publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
