



Operation Number: **GU-L1014**
Year- PMR Cycle: **Second period Jan-Dec 2013**
Last Update: **7/8/2014**
PMR Validation Stage: **Validated by Representative**

Chief of Operations validation date: **07/08/2014**
Division Chief validation date: **07/08/2014**
Country Representative validation date: **07/08/2014**

Inter-American Development Bank - IDB
Office of Strategic Planning and Development Effectiveness

Operation Profile

Basic Data

Operation name:	Establishing Cadastral Registry & Strengthening Legal Certainty Protected Areas	Loan Number:	2149/BL-GU
Executing Agency (EA):	Registro de Información Catastral		
Team Leader:	Milewski,Joseph Christofer	Sector/Subsector:	BIODIVERSITY AND PROTECTED AREAS CONSERVATION
Operation Type:	Loan Operation	Overall Stage:	Disbursing (From eligibility until all the loans are closed).
Lending Instrument:	Investment Loan	Country:	GUATEMALA
Borrower:	REPUBLICA DE GUATEMALA		
		Convergence related Operation(s):	

Total Cost and Source

	Original IDB	Current Active IDB	Local Counterpart	Co-Financing/Country	Total operation cost - Original Estimate
GU-L1014	\$22,000,000.00	\$22,000,000.00	\$0.00	\$0.00	\$22,000,000.00

Available Funds (US\$)

	Current IDB	Disb. Amount to Date	% Disbursed	Undisbursed Balance
GU-L1014	\$22,000,000.00	\$10,295,000.00	46.80%	\$11,705,000.00


Environmental and Social Safeguards

Main Operation	
Impacts Category:	C
Safeguard Performance Rating:	
Safeguard Performance Rating - Rationale:	

Reformulation Information

Main Operation	
Was/Were the objective(s) of this operation reformulated?	NO
Date of approval:	

Expense Categories by Loan Contract (cumulative values)

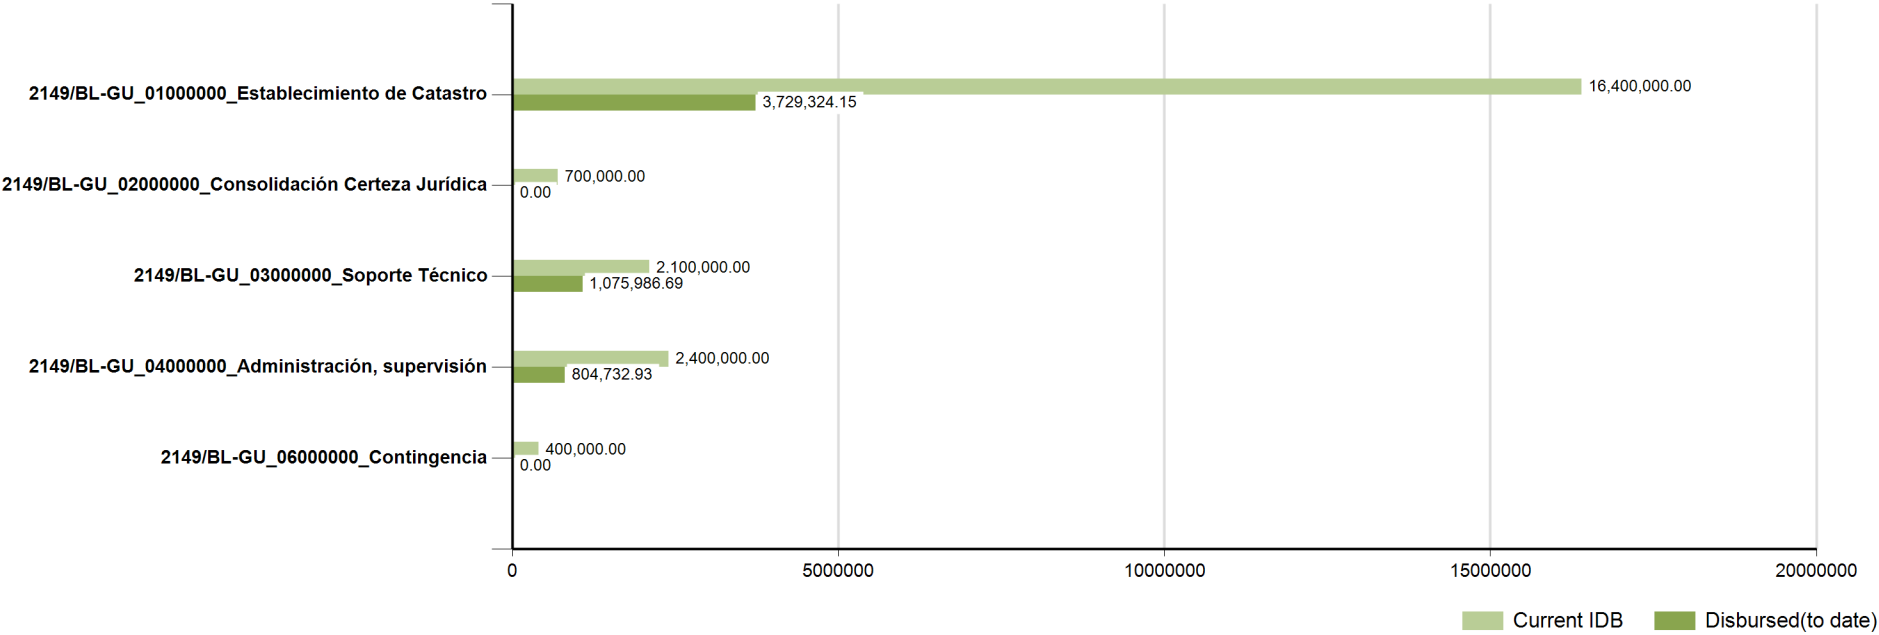

Results Matrix

Impacts

Impact:	1 Las áreas protegidas que conforman el SIGAP cuentan con certeza espacial y jurídica							
Observation:	SIGAP: Sistema Guatemalteco de Áreas Protegidas							
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
1.1 Áreas protegidas con certeza espacial y jurídica		Área protegida	0.00	2009	Documentos de adscripción en el RGP		P	92.00
							P(a)	92.00
							A	

 RF - RF Indicator

 SI - Sector Indicator

 CI - Country Indicator

 PG - Pro-Gender

 PE - Pro-Ethnicity

Outcomes

Outcome:	1 Áreas protegidas de gestión nacional tienen cuentan con establecimiento catastral							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
1.1 Áreas protegidas del SIGAP cuentan con catastro		Área Protegida	0.00	2008	Reportes semestrales del RIC.		P	92.00
							P(a)	92.00
							A	
Outcome:	2 Conflictividad social resultado de la implementación del proceso catastral se reduce							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
2.1 Número de conflictos registrados		Conflictos	0.00	2008	Reportes semestrales del RIC		P	0.00
							P(a)	0.00
							A	
Outcome:	3 Se consolida la certeza jurídica de las áreas protegidas del SIGAP							
Observation:								
Indicators	Flags*	Unit of Measure	Baseline	Baseline Year	Means of verification	Observations	EOP	
3.1 Áreas protegidas registradas en el RGP	 RF	Porcentaje	1.00	2008	Reportes semestrales del RIC. Registros del RGP.		P	92.00
							P(a)	92.00
							A	

 RF - RF Indicator

 SI - Sector Indicator

 CI - Country Indicator

 PG - Pro-Gender

 PE - Pro-Ethnicity

Outputs: Annual Physical and Financial Progress

Catastro en áreas protegidas	Physical	Financial
------------------------------	----------	-----------

Outputs	Unit of Measure	Progress			Progress		
			2013	EOP		2013	EOP
Áreas protegidas cuentan con información registral para el análisis catastral de las fincas dentro de sus límites	Áreas protegida	P	10.00	92.00	P	150,000.00	524,000.00
		P(a)	10.00	20.00	P(a)	150,000.00	301,041.67
		A	17.00	20.00	A	247,916.67	301,041.67
Áreas protegidas con demarcación física y registro de sus límites, incluyendo límites de zonificación interna establecidos por ley	Proyectos	P	10.00	92.00	P	4,400,000.00	12,941,000.00
		P(a)	10.00	20.00	P(a)	3,800,000.00	750,000.00
		A	17.00	20.00	A	437,500.00	750,000.00
Instancia de coordinación interinstitucional organizada y operando con capacidad para el manejo de conflictos asociados al catastro y registro de tierras dentro de las áreas protegidas	Instancia	P	0.00	1.00	P	20,000.00	132,000.00
		P(a)	0.00	1.00	P(a)	20,000.00	3,825.00
		A		1.00	A	2,700.00	3,825.00
Áreas protegidas con estrategia de comunicación implementada	Área protegida	P	10.00	92.00	P	340,000.00	1,114,000.00
		P(a)	10.00	20.00	P(a)	340,000.00	233,750.00
		A	17.00	20.00	A	192,500.00	233,750.00
Base de datos de monitoreo de conflictos	Base de datos	P	0.00	1.00	P	250,000.00	640,000.00
		P(a)	0.00	1.00	P(a)	250,000.00	66,200.00
		A		1.00	A	46,500.00	66,200.00
Áreas protegidas cuentan con establecimiento catastral	Áreas protegidas	P			P		
		P(a)		17.00	P(a)		1,323,402.53
		A	17.00	17.00	A	1,323,402.53	1,323,402.53
Areas protegidas catastradas	Km cuadrado	P			P		
		P(a)		25,986.00	P(a)		10,410,771.18
		A			A		
Areas protegidas con procuracion legal	Area protegida	P			P		
		P(a)		87.00	P(a)		385,540.50
		A			A		
Diagnósticos territoriales de áreas protegidas con información estratégica disponible para la toma de desiciones durante la ejecución del proyecto realizados	Diagnóstico	P	10.00	92.00	P	340,000.00	737,000.00
		P(a)	10.00	0.00	P(a)	180,000.00	697,449.34
		A	0.00	0.00	A	0.00	697,449.34
Areas protegidas delimitadas	Area protegida	P			P		
		P(a)		72.00	P(a)		357,300.00
		A			A		
Areas protegidas demarcadas	Km	P			P		
		P(a)		4,962.74	P(a)		643,121.48
		A			A		
Consolidación de la certeza jurídica de las áreas protegidas		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2013	EOP		2013	EOP
Áreas protegidas cuentan con proceso de procuración legal para el registro, adscripción y anotaciones al final del proyecto	Área Protegida	P	0.00	92.00	P	0.00	828,000.00
		P(a)	0.00	5.00	P(a)	0.00	0.00
		A	5.00	5.00	A	0.00	0.00
Apoyo técnico, coordinación interinstitucional y uso de la información catastral y registral		Physical Progress			Financial Progress		
Outputs	Unit of Measure		2013	EOP		2013	EOP
Convenios interinstitucionales suscritos en el marco del proyecto	Convenio	P	0.00	8.00	P	80,000.00	316,000.00
		P(a)	0.00	9.00	P(a)	50,000.00	72,179.47
		A	5.00	9.00	A	47,179.47	72,179.47

Unidades de apoyo implementadas y con apoyo técnico en instituciones socias del proyecto a partir del segundo año	Unidades	P	4.00	7.00	P	200,000.00	1,597,000.00
		P(a)	4.00	8.00	P(a)	252,000.00	53,778.56
		A	4.00	8.00	A	8,778.56	53,778.56
Diseñar y Construir las bases de datos georeferenciada en materia de catastro y registro, tenencia y uso de la tierra en áreas protegidas.	base de datos	P			P		
		P(a)		0.00	P(a)		22,500.00
		A	0.00	0.00	A	22,500.00	22,500.00
Desarrollo de aplicativos tecnologicos	aplicativos	P			P		
		P(a)		48.00	P(a)		1,109,000.00
		A			A		
Sitios arqueologicos y lugares ceremoniales idigenas verificados (IDAEH)	Sitios	P			P		
		P(a)		323.00	P(a)		56,202.00
		A			A		
Sistema de seguimiento e información de catastro y registro, tenencia y uso de la tierra en áreas protegidas interconectanto RIC / RGP / CONAP en operación	Sistema	P	0.00	1.00	P	1,000,000.00	1,375,000.00
		P(a)	0.00	0.00	P(a)	1,000,000.00	2,500.00
		A	0.00	0.00	A	2,500.00	2,500.00
Delimitacion de reservas territoriales del estado	Km	P			P		
		P(a)		140.00	P(a)		34,125.00
		A			A		
Tierras regularizadas a favor de comunidades (FONTIERRAS)	Comunidades	P			P		
		P(a)		30.00	P(a)		107,366.00
		A			A		
Dictamenes tecnico-juridicos sobre proceso catastral (CONAP)	Dictamenes	P			P		
		P(a)		100.00	P(a)		231,000.00
		A			A		
Administración y seguimiento							

Other Cost		2013	Cost
Administración y seguimiento	P	\$419,000.00	\$2,800,000.00
	P(a)	\$419,000.00	\$1,952,720.00
	A	\$554,269.00	\$578,672.00
Total Cost		2013	Total Cost
	P	\$7,199,000.00	\$23,004,000.00
	P(a)	\$6,461,000.00	\$5,866,193.28
	A	\$2,885,746.23	\$4,105,298.57

Changes to the Matrix

No information related to this operation.

Please note that the Overall Stage represents the stage of the operation at the time of this report's publication, which might not necessarily match the stage of the operation during the PMR Cycle to which the report pertains.
